



REPUBLIC OF GHANA

OPEN GOVERNMENT PARTNERSHIP

5TH NATIONAL ACTION PLAN (NAP 5)

Annual Performance Assessment Report (December 2025)

Table of Contents

1.0 Introduction and Background	3
2.0 Approach and Methodology	5
2.1.2 Data Analysis.....	5
2.2 Reporting	5
3.0 Findings	6
4.0 Conclusion	16

1.0 Introduction and Background

1.1 Introduction

This Annual Performance Assessment Report (APR) has been prepared by the Monitoring and Evaluation (M&E) specialist for the attention of the Steering Committee and other relevant stakeholders of Open Government Partnership (OGP), Ghana. The report summarises performance of the strategic interventions implemented by the Ministries, Departments and Agencies (MDAs) and the Collaborating Civil Society Organisations (CSOs) detailed in the 5th Open Government Partnership (OGP) National Action Plan (NAP 5) 2023-2027 from January 2024 to December 2025. The report also provides updates on progress towards achievement of the twenty-five (25) commitments delineated in the OGP NAP 5, highlights key implementation challenges and lessons learned and provides recommendations aimed at accelerating delivery and impact of the OGP NAP 5 across the public sector of Ghana.

1.2 Overview of the 5th Open Government Partnership (OGP) National Action Plan (2023-2027)

The 5th OGP National Action Plan (NAP 5) 2023-2027 was co-created by the Multi Stakeholder Forum (MSF) comprising government (implementers) and CSOs (Collaborators) in 2022. The OGP NAP 5 represents the strategic priorities and intentions of government and the citizens, in terms of governance reforms most critical for sustained economic growth and durable democratic governance.

Structured around the four pillars of OGP i.e. Transparency, Accountability of public office holders, Participation in governance and the Use of modern technology, the action plan focuses on six (6) thematic areas i.e., Accountability, Transparency, Participation, Technology and Innovation, Open Parliament and Roads and Flagship Health Infrastructure Delivery. There are twenty-five (25) commitments clustered around the six thematic areas, each with a clearly defined set of milestone activities expected to be implemented from January 2024 to December 2027. The government has identified a joint implementation team for each of the commitments task with the responsibility of translating the various commitments into tangible results over the four-year implementation period (2023-2027).

1.3 The Annual Performance Assessment of the 5th Open Government Partnership (OGP) National Action Plan (2023-2027)

In line with its responsibility to monitor, evaluate and report on the performance and impact of Open Government National Action Plans, the secretariat has instituted mechanisms for systematic monitoring, evaluation and reporting on the delivery and impact of the OGP interventions. These mechanisms include performance review meetings with OGP Focal teams of the participating MDAs, and conduct of quarterly and annual performance assessment of National Action Plans. The 2025 Annual Performance review was therefore conducted in line with the mandate of the secretariat and is intended to gauge the performance of the OGP NAP 5 including achievement of 2024-2025 performance targets.

1.4 Objectives of the Assessment

The aim of the 2025 Annual performance review was to assess performance of the implementing entities relative to implementation the 2024-25 milestone activities and report on progress towards achievement of the 25 commitments detailed in the OGP NAP 5. Specifically, the review sought to:

- Assess progress towards achievement of commitments outlined in the OGP NAP 5
- Evaluate progress of implementation of the 2024 and 2025 milestone activities and targets detailed in the 5th OGP National Action Plan);
- Identify and document emerging issues including key implementation challenges and lessons learned; and
- Provide recommendations that can inform management decisions on promoting timely implementation and achievement of the expected results.

1.5 Key Assessment Questions

To guide the review, the following questions were developed:

1. What was the overall performance of the NAP 5 as end of December 2025?
2. What is the status of implementation of planned milestone activities and performance of the commitments detailed in the NAP over the reporting period.;
3. What were the key implementation challenges that had to be brought to the attention of the Steering Committee and other stakeholders?

2.0 Approach and Methodology

The assessment employed a participatory and utilisation focused approach aimed at generating evidence-based information that will promote learning and accountability for results across the different actors of the Open Government Partnership Initiative.

The assessment followed a three-stepped approach:

2.1 Data Collection and Analysis

2.1.1 Data Collection

This stage of the process involved collection, collation, validation and analysis of performance data provided by the implementing MDAs. As part of the process, copies of agreed data collection forms were shared with the MDAs for the compilation of performance updates and the targets achieved as at the end of September 2025. Follow-up discussion and reviews mainly by phone or email were held with the focal persons to clarify and or gather additional information. The data submitted by the Ministries were carefully reviewed and validated for consistency, reliability and alignment with the NAP 5.

2.1.2 Data Analysis

The following analytic approaches were used to gauge the performance of the NAP 5 relative to progress towards achievement of the commitments and effective implementation of the milestone activities over the period under review.

- A Meta-Analytic approach was used to aggregate data on the different performance indicators to determine the overall performance for the years under review;
- Colour coded performance in terms of achievement of milestone of the respective focus areas of the six thematic areas; and
- Descriptive analysis - providing general statistics and understanding of the information generated and their underlying assumptions.

2.2 Reporting

The performance monitoring report is composed of a narrative section that summarises the performance of the focus areas and a colour-coded dashboard of the performance of milestone activities delineated in the NAP 5 as at the end of September 2025.

The colour-coded dashboard is categorised as follows:

- **Green:** Target Achieved (Activity Completed)
- **Amber:** Target Not Achieved (Activity Ongoing)

- **Red:** At Risk because of operational or external factors beyond the implementers' control (Activity not started or stuck due challenges beyond implementers' control)
- **Grey:** Unreported

The report highlights emerging issues and summarises recommendations that can help strengthen the delivery and impact of OGP 5th National Action Plan.

2.4 Limitations

Delayed submission of performance updates by the implementing MDAs constituted the main limitation to the review exercise.

3.0 Findings

This section of the report details the key findings of the Annual performance assessment. It aggregates cumulative performance of the MDAs relative to implementation of the 2024 and 2025 milestone activities and the extent of progress towards the 25 reform commitments detailed in the OGP NAP 5.

3.1. Progress Towards Achievement of Commitments

In general, the commitments are on track and the implementing entities have made significant progress towards achieving the 25 commitments set out in the OGP NAP 5 as at November 2025. Eighteen (13) commitments are on track and are rated “**Green**” indicating substantial progress towards achievement of the commitments. 3 commitments and were rated “**Amber**” indicating good progress by the MDAs towards achieving the commitments although implementation of some of the milestone activities under them were still ongoing. Save for Component 3 commitments notably the Citizen Complaints Centre, Misinformation and Disinformation and Justice that are either experiencing delays in implementation or yet to start and are rated “**Red**” indicating that the commitments risk not attainment at the end of the implementation period. Save for three commitments mentioned above, all the other commitments have made significant progress and are likely to be delivered at the end of December 2027. (See table 1 below for detailed update on status per each of the commitments). Figure 1 and the commitment tracker below provide details of progress towards the commitments:

Figure 1: Commitments

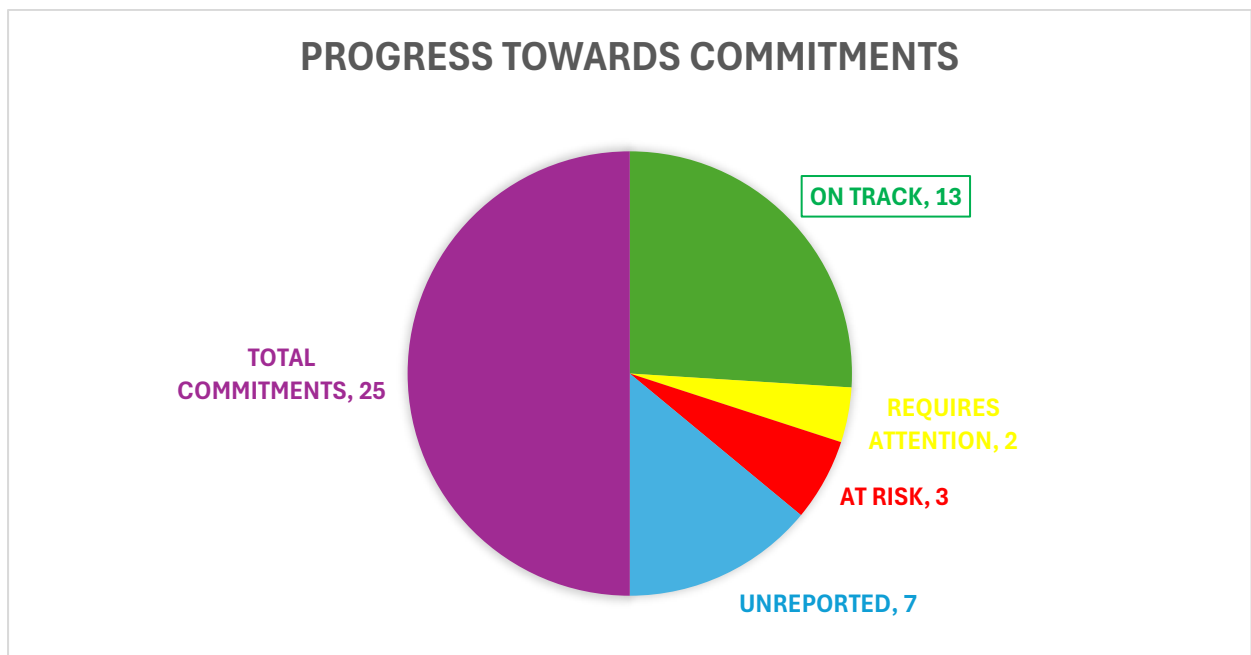


Table 1: COMMITMENT PERFORMANCE TRACKER

Focus Area	Commitment					Colour Code	Remarks
		On Track	Requires Attention	At Risk	Unreported		
Asset Declaration	1. Pass the Conduct of Public Officers bill into law, ensuring that provisions on assets declaration require verification and come with severe sanctions for non-compliance.				No Data		No Data
	2. Develop regulations to fully operationalise the Conduct of Public Officers' bill when passed into law				No Data		
	3. Publish a Public Financial Management Compliance League Table for Public Institutions and apply the necessary sanctions as stated in the PFM Act for non- compliance.				No Data		
Witness Protection	4. Provide effective protection for persons who are exposed to danger for witnessing in criminal prosecutions, by passing regulations to the Witness Protection Act and setting up the Witness Protection Agency				No Data		No Data
Public Accounts Committee and Audit Report Implementation	5. Ensure effective implementation of Audit recommendations from Internal Auditors, External Auditors, Audit Committees and of Public Accounts Committee on the reports of the Auditor-General and Management Letters by Public Institutions by building the capacity of Internal Audit Units (IAUs) Audit Committees, Heads and Boards Public Institutions to implement the new Audit Report Recommendations and Implementation Instructions (ARR&I).	On Track					Substantial progress
Anti-money Laundering and Combating Terrorism Financing (AML/CTF	6. To effectively implement the Anti-Money Laundering Act, 2020 (Act 1044) to ensure that Ghana does not get blacklisted again for lapses in the country's AML/CTF regime	On Track					Substantial progress

Enabling CHRAJ's Administrative Justice Delivery Mandate	7. To develop a comprehensive online/web-based complaint and redress system on all mandate areas of the Commission to enable it perform its administrative justice delivery mandate better		Requires Attention				Good Progress
Health Service Delivery	8. Ensure greater accountability in the health sector by establishing digital platforms to facilitate complaints and feedback on quality-of service delivery	On Track					Substantial Progress
	9. Uncap the NHIA funds to ensure prompt disbursement and release of NHIA allocations to primary healthcare centres.	On Track					Substantial Progress
Power Purchasing Agreements	10. Amend the PURC Act to expand its mandate to include public disclosure of PPAs.	On Track					Substantial Progress
Right to Information	11. Create public awareness on the RTI Act, how it operates and obligations of public institutions.	On Track					Substantial Progress
	12. Pass Regulations to fully operationalise the RTI Act.	On Track					Substantial Progress
	13. Provide adequate funding for the implementation of the RTI Act				No Data		No Data
Fisheries	14. Pass a new Fisheries Act or amend the existing one to provide for greater transparency in the fisheries sector.	On Track					Substantial Progress
Justice	15. Pass the Community Service Bill into Law by 2026.			At risk			No Progress
Citizens' Complaints Centre	16. Establish a coordinated and syndicated citizen feedback mechanism on public policy and public service delivery.			At risk			No Progress
Gender Equality	17. Ensure the progressive increase in women's political participation at all levels of government, by passing the Affirmative Action Bill into law.	On Track					Substantial Progress
Citizen Participation in Local Government	18. Enhance Citizens' Participation in Local Gov't through election of MMDCEs.		Requires Attention				Good Progress
Misinformation and Disinformation	19. Implement structures to combat Misinformation / Disinformation on digital platforms.			At Risk			No Progress

Data Sharing and Intermediation of Public Service Delivery Platforms	20. Strengthen Data sharing and intermediation among public service delivery platforms.		Requires Attention				Good Progress
Open Parliament	21. Establish oversight mechanism in parliament to ensure achievement of the national OGP commitments	On Track					Substantial Progress
	22. Enhance access to information on parliament's work in an easily accessible, user friendly, and timely manner.	On Track					Substantial Progress
	22. Increase engagement between Parliament and citizens.	On Track					Substantial Progress
Infrastructure Policy	23. Enhance transparency and foster public trust by providing access to road contracts, data on road infrastructure projects, facilitating participatory monitoring, and informed citizens' engagement in decision-making processes in the road infrastructure policy area.				No Data		No Data

3.2 Progress of Implementation of Milestone Activities

The aggregate performance of the MDAs in terms of implementation of the 2024 and 2025 milestone activities stands at 61% (Green+ Amber). 27 activities translating to 47% had been completed at the time of the review. 8 (14%) activities were in progress, 10 (18%) had not started at the time of the assessment. However, there was no data to assess 12 activities. (Details in the tables 2, 4 and 4 below)

- 27 out of 57 representing 47% of the Milestone activities assessed were completed at the time of the review.
- The number of ongoing activities 8 representing 14%
- 10 activities translating to 18% had either not started or were stuck
- There was no response on extent of implementation 12 activities representing 21%

Figure 2:



Table 2: LIST OF COMPLETED 2024-25 MILESTONNE ACTIVITIES

Focus Area	Milestone Activity	Status	Colour Code
Public Account Committee and Audit Report Implementation	1. Develop Framework for the Public Financial Management Compliance (PFM) League Table	Completed	
	2. Develop Training manual for training audit committees on basic accounting and records keeping	Completed	
	3. Conduct training for Audit Committees, Internal Audit Units and Heads of Public Institutions	Completed	
Anti-money Laundering and Combating Terrorism Financing (AML/CTF)	4. Hold Stakeholder consultations for the development of regulations	Completed	
	5. Pass Regulations to the Companies Act, 2019 (Act 992) particularly provisions on BO	Completed	
	6. Organize Awareness creation events among relevant stakeholders	Completed	
	7. Train Competent authorities in detecting AML/CTF risks	Completed	
Enabling CHRAJ's Administrative Justice Delivery Mandate	8. Develop Web-based system	Completed	
Health Service Delivery	9. Established digital platforms commissioned and operationalised by Government	Completed	
	10. Serve Notice of government intent to uncap the NHIA fund	Completed	
	11. Pilot the established Digital platforms	Completed	
	12. Develop Draft amendment bill to uncap NHIA	Completed	
Power Purchasing Agreements	13. Establish Modalities for the disclosure of Power Purchasing Agreements (PPAs)	Completed	
	14. Develop Registry to hold and publish relevant data on PPAs	Completed	
Right to Information	15. Develop IEC materials on RTI	Completed	
	16. Draft Regulations to fully operationalize RTI Act	Completed	
	17. Initiate public awareness and public education	Completed	
Fisheries	18. Develop Draft Fisheries Act or amend existing Act	Completed	
	19. Hold Stakeholder engagement on draft Bill or amended Bill	Completed	
Gender Equality	20. Organise Stakeholder consultation on the Affirmative Action Bill across the country	Completed	

	21. Review the Affirmative Action Bill for Cabinet approval	Completed	
Citizen Participation in Local Government	22. Adopt National Accessibility Strategy to guide the implementation of accessibility standards for PWDs and the aged		
Data Sharing and Intermediation of Public Service Delivery Platforms	23. Train stakeholders on the government enterprise architecture and interoperability framework document	Completed	
	24. Enhance Infrastructure for licensing/ Certificate Authorities to be able to roll	Completed	
Open Parliament	25. Build Capacity of OGP Caucus Members on OGP and Open Parliament	Completed	
	26. Establish an Open Parliament Steering Committee which follows OGP standards	Completed	
	27. Operationalise the Open Parliament Steering Committee which follows OGP standards		

Table 3: LIST OF 2024-25 MILESTONNE ACTIVITIES (Implementation in Progress)

Focus Area	Milestone Activity	Status	Colour Code
Enabling CHRAJ's Administrative Justice Delivery Mandate	1. Network CHRAJ offices nationwide	In Progress	
Justice	2. Submit Cabinet memo to Cabinet for approval	In Progress	
Citizen Participation in Local Government	3. Facilitate consensus on amendment of article 55 (3) to allow political parties to sponsor candidates to local level election	In Progress	
Misinformation and Disinformation	4. Develop Framework on Media literacy /Public Education, Fact Checking activities	In Progress	
Data Sharing and Intermediation of Public Service Delivery Platforms	5. Develop Integration and Data Sharing Framework	In Progress	
Open Parliament	6. Undertake engagements between OGP Caucus members and OGP stakeholders	In Progress	

Table 4: LIST OF 2024-25 MILESTONNE ACTIVITIES (Implementation not Started)

LIST OF 2024-25 MILESTONNE ACTIVITIES AT RISK (Not Started)			
	Milestone Activity	Status	Colour Code
Right to Information	1. Lay Regulations before parliament	At Risk	
Justice	2. Lay draft Bill before Parliament	At Risk	
	3. Submit the approved Bill to Parliament	At Risk	
	4. Commission L.I and Paralegal Framework to the Office of the Attorney General for comments	At Risk	
Citizens' Complaints Centre	5. Complete Institutional Arrangements and Preparatory Activities	At Risk	
	6. Complete Implementation of Pilot Phase of the Citizen Complaint Mechanism	At Risk	
Citizen Participation in Local Government	7. Pass Persons with Disability Re-enactment Bill and the accompanying legislative instruments	At Risk	
	8. Hold referendum on proposed amendments	At Risk	
Misinformation and Disinformation	9. Develop Terms of Reference for Human Rights Assessment	At Risk	
	10. Pilot Framework on Media Literacy/Public Education, Fact Checking	At Risk	
	11. Initiate Human Rights assessment of existing legislation on disinformation to ensure they are not used to stifle free speech	At Risk	
Open Parliament	12. Conduct Baseline survey on citizens access to Parliamentary Information	At Risk	

Priorities for the Next 12 Months

Table 4: Highlights of some selected milestone activities that needs to be re- prioritized during the 2026 implementation period.

Table 5: FOCUS FOR THE NEXT TWELVE MONTHS

Focus for the Next 12 Months	
Component	Priority
Asset Declaration	1. Draft Conduct of Public Officers' Bill approved by Cabinet
	2. Develop Framework for the Public Financial Management Compliance (PFM) League Table
	3. Finalise and submit a Final Draft Conduct of Public Officers' Bill
	4. Hold Public Consultation on the Draft
Witness Protection	5. Develop Regulations to fully operationalize the Witness Protection Act
	6. Pass Regulations to the Witness Protection Act
Public Accounts Committee and Audit Report Implementation	7. Organize training for MDAs in the various zones
Enabling CHRAJ's Administrative Justice Delivery Mandate	8. Network CHRAJ offices nationwide
Right to Information	9. Provide adequate funding for the implementation of the RTI Act
Justice	10. Submit Cabinet memo to Cabinet for approval

4.0 Conclusion

The OGP NAP 5 has made significant progress towards achievement of the 25 commitments. Implementation rate is estimated at 62% and the implementing entities are likely to achieve most of the outstanding deliverables before the end of the 2027. Save for Commitment on Asset Declaration and Citizen protection that have experienced delays in terms of meeting the expected targets, the other commitments have made significant progress.

A number of challenges and lesson were also documented in the course of the review, key among them is: inadequate funding; political transition; and inadequate communication and change management.

The above notwithstanding, it can be concluded the OGP NAP 5 is on track and likely to achieve all the planned deliverables if the current momentum is maintained and implementation challenges mitigated and emerging opportunities incorporated into the management.

ACCOUNTABILITY											
Progress of Implementation of 2024 and 2025 Milestone Activities											
Focus Area	Milestone(s) (2024 Targets)	Timeline		Status				Description of Status	Means of Verification	Colour Code	Remarks
		Jan	Dec	Completed	In progress	Not started	Unreported				
Asset Declaration											
Commitment: Pass the Conduct of Public Officers bill into law, ensuring that provisions on assets declaration require verification and come with severe sanctions for non-compliance.											No Data
Develop regulations to fully operationalise the Conduct of Public Officers’ bill when passed into law											No Data
Publish a Public Financial Management Compliance League Table for Public Institutions and apply the necessary sanctions as stated in the PFM Act for non-compliance.											No Data
	Draft Conduct of Public Officers’ Bill approved by Cabinet	2024	2024				Unreported				
	Develop Framework for the Public Financial Management Compliance (PFM) League Table	2024	2024				Unreported				
	Finalise and submit a Final Draft Conduct of Public Officers’ Bill	202	202				Unreported				
	Hold Public Consultation on the Draft	2025	2025				Unreported				

Witness Protection											
Commitment: Provide effective protection for persons who are exposed to danger for witnessing in criminal prosecutions, by passing regulations to the Witness Protection Act and setting up the Witness Protection Agency											
	Develop Regulations to fully operationalize the Witness Protection Act	2024	2024				Unreported				
	Pass Regulations to the Witness Protection Act	2025	2025				Unreported				
Public Accounts Committee and Audit Report Implementation											
Commitment: Ensure effective implementation of Audit recommendations from Internal Auditors, External Auditors, Audit Committees and of Public Accounts Committee on the reports of the Auditor-General and Management Letters by Public Institutions by building the capacity of Internal Audit Units (IAUs) Audit Committees, Heads and Boards Public Institutions to implement the new Audit Report Recommendations and Implementation Instructions (ARR&I).											Commitment on Track
	Develop Framework for the Public Financial Management Compliance (PFM) League Table			Completed				The development of Guidelines for Implementation of PFM Commitment Control and Expenditure Management Measures for Ministries, Departments and Agencies were prepared and issued	Guidelines for Implementation of PFM Commitment Control and Expenditure Management Measures for Ministries, Departments and Agencies		Target Met

								on the 2 nd of May, 2025 under the signature of the Hon Minister for Finance	issued on 2 nd May 2025 by Dr Cassiel Ato Forson (MP) Minister for Finance		
	Develop Training manual for training audit committees on basic accounting and records keeping			Completed				Guidelines on Audit Committee developed-2023 and signed by the Minister of Finance			Target Met
	Organize training for MDAs in the various zones						Unreported				
	Conduct training for Audit Committees, Internal Audit Units and Heads of Public Institutions			Completed				110 Audit Committee Secretaries were trained in record keeping in 2024			Target Met
Anti-money Laundering and Combating Terrorism Financing (AML/CTF)											
Commitment: To effectively implement the Anti-Money Laundering Act, 2020 (Act 1044) to ensure that Ghana does not get blacklisted again for lapses in the country's AML/CTF regime											Commitment on Track
	Hold Stakeholder consultations for			Completed				FIC organised a two-day sensitisation	Attendance from the		Target Met

	the development of regulations							workshop for over 200 stakeholders on the draft regulations for the Anti Money Laundering Act, 2020 (ACT 104)	stakeholder engagement organised on the 3rd-4th September at Alisa Hotel, Accra		
	Pass Regulations to the Companies Act, 2019 (Act 992) particularly provisions on BO			Completed				Ghana has passed specific regulations relating to beneficial ownership (BO) under the Companies Act, 2019 (Act 992). The primary regulation is the Companies (Beneficial Ownership Information) Regulations, 2020 (L.I. 2409, or simply the Companies Regulations, 2023 (L.I 2473) These regulations operationalise the beneficial ownership disclosure requirements mandated by Act 992 and establish a Central Register for beneficial ownership data, maintained the office of the Registrar of companies.	Companies Regulations, 2023 (L.I 2473)		Target Met

	Organize Awareness creation events among relevant stakeholders			Completed				FIC organised a stakeholder workshop to disseminate findings of the various Risk Assessment Reports (NRA & Other Risks assessments). The forum was also used to update stakeholders on the third-round mutual evaluation process	Attendance Sheets		Target Met
	Train Competent authorities in detecting AML/CTF risks			Completed				Competent authorities in detecting AML/CTF risks			Target Met
Enabling CHRAJ's Administrative Justice Delivery Mandate											
Commitment: To develop a comprehensive online/web-based complaint and redress system on all mandate areas of the Commission to enable it perform its administrative justice delivery mandate better											Commitment requires attention
	Develop Web-based system			Completed				The system has been piloted at the Head office since 9/9/2024. The Web based system is currently in use	The domain name is: www.cms.chraj.gov.gh		Target Met
	Network CHRAJ offices nationwide				In Progress			The equipment for implementing the project has been			Target in Progress

								purchased. Additionally, the procurement process for selecting a network consultant to commence the project is in progress. The network infrastructure project will commence in the 4th Quarter.			
Health Service Delivery											
Commitment: Ensure greater accountability in the health sector by establishing digital platforms to facilitate complaints and feedback on quality-of service delivery											Commitment is on Track
Uncap the NHIA funds to ensure prompt disbursement and release of NHIA allocations to primary healthcare centres.											Commitment is on Track
	Established digital platforms commissioned and operationalised by Government			Completed				Ghana has established digital platforms to facilitate complaints and feedback on healthcare quality delivery	NeHSA Telehealth Platform: The National Health Insurance Authority (NHIA) is piloting a new telehealth platform (NeHSA) to improve access to healthcare services through digital means		Target Met

									GHIMS Electronic Health Records: The Ministry of Health has announced a new-fully state-owned digital health platform, the Ghana Health Information Management System (GHIMS), to replace the previous Lightwave Health Information Management System (LHIMS)		
--	--	--	--	--	--	--	--	--	--	--	--

TRANSPARENCY											
Progress of Implementation of 2024 Milestone Activities											
Focus Area	Milestone(s) (2024 Targets)	Timeline		Status				Description of Status	Means of Verification	Colour Code	Remarks
		Jan	Dec	Completed	In progress	Not started	Unreported				
Power Purchasing Agreements											

Progress of Implementation of 2024 Milestone Activities

Focus Area	Milestone(s) (2024 Targets)	Timeline		Status				Description of Status	Means of Verification	Colour Code	Remarks
		Jan	Dec	Completed	In progress	Not started	Unreported				
Power Purchasing Agreements											

Commitment: Amend the PURC Act to expand its mandate to include public disclosure of PPAs.											Commitment on Track
	Establish Modalities for the disclosure of Power Purchasing Agreements (PPAs)	2024	2024	Completed				In October 2025, Ghana enacted a new law-legislative instrument (LI 2508) requiring all future generation projects to be procured through competitive bidding, a major step toward greater transparency and efficiency	Energy Commission (Planning and Competitive Procurement of Additional Electricity Generation Capacity Regulations, 2025		Target Met
	Develop Registry to hold and publish relevant data on PPAs	2025	2025	Completed				The register to hold and publish relevant data on PPAs developed	https://www.purc.com.gh/catalog/resources/subcategories/register-of-power-purchase-agreements		Target Met
Right to Information											
Commitment: Create public awareness on the RTI Act, how it operates and obligations of public institutions.											Commitment on Track
Pass Regulations to fully operationalise the RTI Act.											Commitment on Track
Provide adequate funding for the implementation of the RTI Act											
	Develop IEC materials on RTI	2024	2024	Completed				IEC materials on RTI developed Printed IEC materials are being used by the	Sample IEC Materials		Target Met

								Commission for training and sensitisation activities			
	Draft Regulations to fully operationalize RTI Act	2024	2024					Draft Regulations ready for pre-laying sessions with the Subsidiary Legislation Committee of Parliament and the Attorney General's office.			Target Met
	Initiate public awareness and public education	2025	2025	Completed				The Commission has undertaken 31 traditional media engagements, 160 social media engagements and 81 public institution sensitisations as part of its efforts towards public awareness and education.			
	Lay Regulations before parliament	2025	2025	Completed		Not Started		Draft Regulations yet to be laid before parliament			Target not Met
Fisheries											
Commitment: Pass a new Fisheries Act or amend the existing one to provide for greater transparency in the fisheries sector.											Commitment on Track
	Develop Draft Fisheries Act or amend existing Act	2024	2024	Completed				The Fisheries and Aquaculture Act, 2025 was developed, passed by Parliament and assented to by the President as August 14 th 2025	Invitation to participate in stakeholder engagement on the Draft Fisheries and		Target Met

									Aquaculture Bill		
	Hold Stakeholder engagement on draft Bill or amended Bill	2025	2025	Completed				Extensive consultations and engagements were held with stakeholders at all levels including government institutions, industry actors, artisanal fishers, and civil society, ensuring that the perspectives of all key groups were reflected in the drafting process	Invitation to Stakeholder Engagement meeting Stakeholder Engagement Reports Fisheries Bill 2025 memorandum		Target Met
Justice											
Commitment: Pass the Community Service Bill into Law by 2026.											Commitment at Risk
	Submit Cabinet memo to Cabinet for approval	2025	2025		In Progress			Drafting of Memo is completed. However, the Memo is yet to be submitted to Cabinet approval			Target Requires attention
	Lay draft Bill before Parliament	2025	2025			Not Started		Activity is dependent on approval of the memo by cabinet			Target Not Met
	Submit the approved Bill to Parliament	2025	2025			Not Started					Target Not Met
	Commission L.I and Paralegal Framework to the Office of the	2025	2025			Not Started		L.I and Paralegal Framework yet to be submitted the Office of the Attorney			Target not Met

	Attorney General for comments							General for comments			
--	----------------------------------	--	--	--	--	--	--	-------------------------	--	--	--

PARTICIPATION											
Progress of Implementation of 2024 and 2025 Milestone Activities											
Focus Area	Milestone(s) (2024 Targets)	Timeline		Status				Description of Status	Means of Verification	Colour Code	Remarks
		Jan	Dec	Completed	In progress	Not started	Unreported				
Citizens' Complaints Centre											
Commitment: To establish a coordinated and syndicated citizen feedback mechanism on public policy and public service delivery.											Commitment at Risk
	Complete Institutional Arrangements and Preparatory Activities	2024	2024			Not Started		As far as CHRAJ is concerned this is an activity that ought to be led by the Ministry of Information. Unfortunately, we are yet to receive direction from the Ministry. We recommend that the Secretariat ought to engage the new Minister to brief him on the activity and to encourage him to play leadership role.			Target Met
	Complete Implementation of	2025	2025			Not Started		As far as CHRAJ is concerned this is an			Target not Met

	Pilot Phase of the Citizen Complaint Mechanism							activity that ought to be led by the Ministry of Information. Unfortunately, we are yet to receive direction from the Ministry. We recommend that the Secretariat ought to engage the new Minister to brief him on the activity and to encourage him to play leadership role.			
Gender Equality											
Commitment: Ensure the progressive increase in women’s political participation at all levels of government, by passing the Affirmative Action Bill into law.											Commitment on Track
	Organise Stakeholder consultation on the Affirmative Action Bill across the country	2024	2024	Completed				Following the passage of the Affirmative Action Act, the Gender Equity Committee has been inaugurated. 2 Gender Equity Meeting held. Sensitisation of the Act ongoing, currently			Target Met
	Review the Affirmative Action Bill for Cabinet approval	2025	2025	Completed				The reviewed Affirmative Action Bill was approved by Cabinet in September 2026 and Parliament passed the	Affirmative Action (Gender Equity) Act 2024		Target Met

								Affirmative Action (Gender Equity) Act 2024 in November 2025			
--	--	--	--	--	--	--	--	---	--	--	--

OPEN PARLIAMENT													
Progress of Implementation of 2024 and 2025 Milestone Activities													
Focus Area	Milestone(s) (2024 Targets)	Timeline		Status				Description of Status	Means of Verification	Colour Code	Remarks		
		Jan	Dec	Completed	In progress	Not started	Unreported						
Open Parliament													
Commitment: Establish oversight mechanism in parliament to ensure achievement of the national OGP commitments.											Commitment on Track		
Enhance access to information on parliament’s work in an easily accessible, user friendly, and timely manner.											Commitment on Track		
Increase engagement between Parliament and citizens.											Commitment on Track		
	Build Capacity of OGP Caucus Members on OGP and Open Parliament	2024	2024	Completed				Capacity of Twenty-six (26) OGP members have been built on OGP	Attendance Sheets indicating the number of OGP Caucus Members trained on		Target Met		

									OGP trained and Open Parliament attached		
	Establish an Open Parliament Steering Committee which follows OGP standards	2024	2024	Completed				An Open Parliament Steering Committee which follows OGP standards established	Evidence found in Page 14 of the Open Parliament Action Plan uploaded at Parliament's website		Target Met
	Operationalise the Open Parliament Steering Committee which follows OGP standards	2025	2025	Completed				Open Parliament Steering Committee which follows OGP standards operationalised	Page 14 of the Open Parliament Action Plan uploaded at Parliament's website		Target Met
	Undertake engagements between OGP Caucus members and OGP stakeholders	2025	2025		In Progress			Initial discussions on a working retreat held			Target in Progress
	Conduct Baseline survey on citizens access to Parliamentary Information	2025	2025			Not Started		The target is not likely to be met. The activity is expected to be completed end of December 2025. Yet the activity has not started three			Target at risk

Citizen Participation in Local Government											
Commitment: Enhance Citizens’ Participation in Local Gov’t through election of MMDCEs.											Commitment Requires attention
	Facilitate consensus on amendment of article 55 (3) to allow political parties to sponsor candidates to local level election	2024	2024		In Progress			The National Constitution Review Committee is considering the election of MMDCEs The Ministry in 2024 reviewed the Decentralisation Policy Framework and Strategy (DPFS) to adopt the election of MMDCES politically.			Target in Progress
	Pass Persons with Disability Re-enactment Bill and the accompanying legislative instruments	2024	2024			Not Started		Persons with Disability Reenactment Bill and its accompanying legislative instruments have not been passed A new disability bill intended to replace the 2006 Act has been in development for			Target not Met

								some time due the original laws limitations			
	Hold referendum on proposed amendments	2025	2025			Not Started					Target not Met
	Adopt National Accessibility Strategy to guide the implementation of accessibility standards for PWDs and the aged	2025	2025	Completed				The National Accessibility Strategy to guide the implementation of accessibility standards for PWDs and the aged was adopted by Ghana in 2025			Target Met

TECHNOLOGY AND INNOVATION											
Progress of Implementation of 2024 and 2025 Milestone Activities											
Focus Area	Milestone(s) (2024 Targets)	Timeline		Status				Description of Status	Means of Verification	Colour Code	Remarks
		Jan	Dec	Completed	In progress	Not started	Unreported				
Misinformation and Disinformation											
Commitment: Implement structures to combat Misinformation / Disinformation on digital platforms.											Commitment at Risk
	Develop Framework on Media literacy /Public	2024	2024		In Progress			The framework has been developed pending cabinet approval			Target in Progress

	Education, Fact Checking activities										
	Develop Terms of Reference for Human Rights Assessment	2024	2024			Not Started		The Terms of Reference will be developed after approval of the framework.			Target not Met
	Pilot Framework on Media Literacy/Public Education, Fact Checking	2025	2025			Not Started		Activity will commence after approval of the framework by cabinet.			Target not Met
	Initiate Human Rights assessment of existing legislation on disinformation to ensure they are not used to stifle free speech	2025	2025			Not Started		Activity will commence after approval of the framework by cabinet			
Data Sharing and Intermediation of Public Service Delivery Platforms											
Commitment: Strengthen Data sharing and intermediation among public service delivery platforms.											
	Develop Integration and Data Sharing Framework	2024	2024		In Progress			Draft Integration and Data Sharing Framework developed. However, the framework is yet			Target Met

								to be finalised due to funding challenges			
	Train stakeholders on the government enterprise architecture and interoperability framework document	2024	2024	Completed				Training conducted for key stakeholders on the government enterprise architecture and interoperability framework document			Target Met
	Operationalise the Integration and Data Sharing Framework	2025	2025		In Progress			Process of formation of National Data Sharing Steering Committee Ministry of Finance is facilitating support from the South Korean Government			Target in Progress
	Enhance Infrastructure for licensing/ Certificate Authorities to be able to roll	2025	2025	Completed				Infrastructure for licensing/ Certificate Authorities is enhanced and digital IDs and verifications rolled out Key stakeholders including BoG, GRA, SIC, PPA, and a lot of regulators and			Target Met

								institutions have been already been met			
--	--	--	--	--	--	--	--	---	--	--	--

ROADS AND HEALTH INFRASTRUCTURE											
Progress of Implementation of 2024 and 2025 Milestone Activities											
Focus Area	Milestone(s) (2024 Targets)	Timeline		Status				Description of Status	Means of Verification	Colour Code	Remarks
		Jan	Dec	Completed	In progress	Not started	Unreported				
Infrastructure Policy											
Commitment: Enhance transparency and foster public trust by providing access to road contracts, data on road infrastructure projects, facilitating participatory monitoring, and informed citizens’ engagement in decision-making processes in the road infrastructure policy area.											No Data
Develop and implement a robust transparency mechanism for flagship health infrastructure projects that ensures public disclosure of project											No Data
	Establish functional, centralized roads and flagship health infrastructure dashboard integrated with real-time project monitoring capabilities, adhering to infrastructure data standards and aligned with existing laws	2025	2025				Unreported				No Data
	Develop Accountability framework tailored to roads and flagship health infrastructure	2025	2025				Unreported				No Data

	projects, outlining processes for data disclosure, social audits and participatory evaluation										
	Organise Stakeholder consultation meetings to validate the framework for roads and flagship health infrastructure with input from government, civil society, and private sector actors	2025	2025				Unreported				No Data
	Finalise Accountability framework for roads and flagship health infrastructure projects	2025	2025				Unreported				No Data
